



Construction Update for the Week of November 5




Crews plan to **shift Main Street traffic** onto the new pavement between the Bypass and Washington Street early next week. This shift will allow crews to begin removing the old sidewalk and pavement on the west side of Main Street in this section.

North of Washington Street crews plan to complete the construction of planters and curbs on the west side of Main Street. The curb placement is designed to accommodate new parallel parking stalls that will replace the old diagonal parking. This traffic calming strategy will create a safer environment for pedestrians and bicyclists. The concrete base for sidewalk pavers will also be poured this week.

Additional work on the west side of Main Street includes the start of the transformation of the Historic Village Hall plaza. Installation of electrical elements for the plaza is the first step in creating this new community gathering place.

As a reminder, northbound traffic continues one-way north of Washington Street to the temporary ramp next to Crystal Creek to access Harrison Street. Drivers will experience new pavement on the east side of Main Street north of Washington Street.

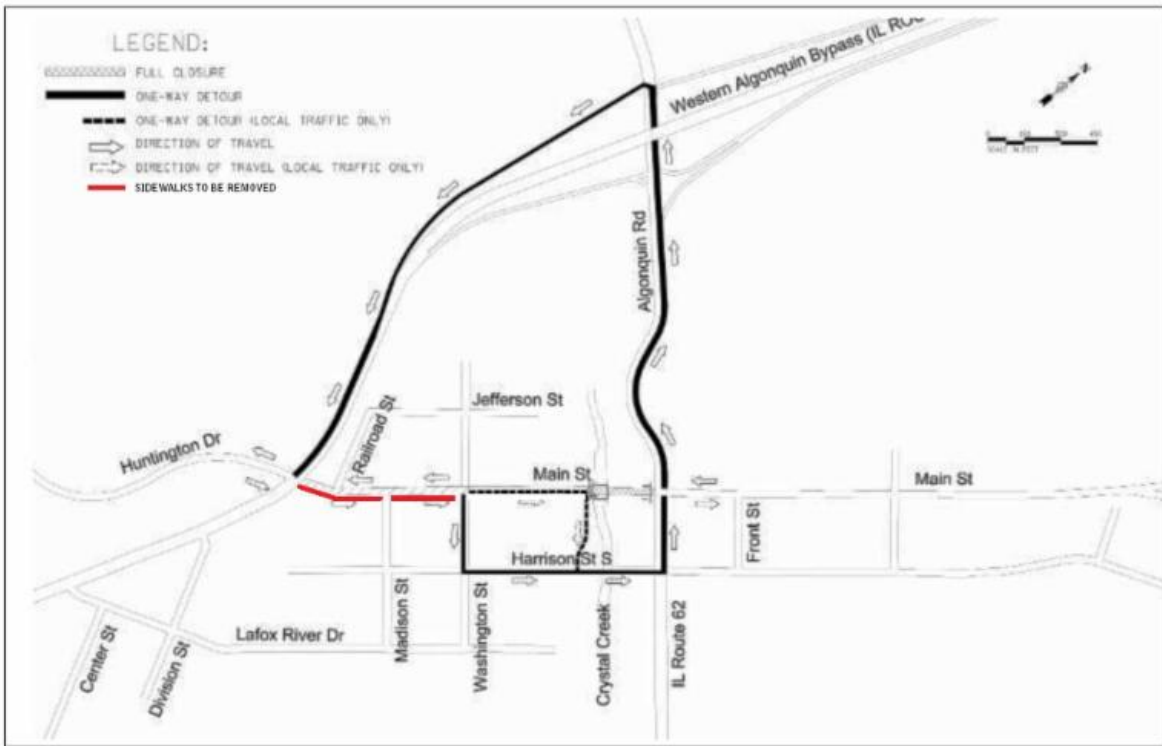

Thank you to everyone who has participated in the Coffee with the Contractor events. We hope you found these meetings informative and helpful in addressing your concerns.
