




## Construction Update for the Week of March 4



Crews will remove the bridge deck (roadway portion of the bridge) surface throughout the week. The removal process will include saw work on Wednesday as crews prepare sections of the structure for removal. Please note that the saw work may cause some noise disruption and dust in the downtown on Wednesday.

On Monday, workers will also begin sawing into the roadway on Main Street north of Algonquin Road. This work needs to be completed so that crews can begin work on the underground sanitary sewer replacement by the end of the week.

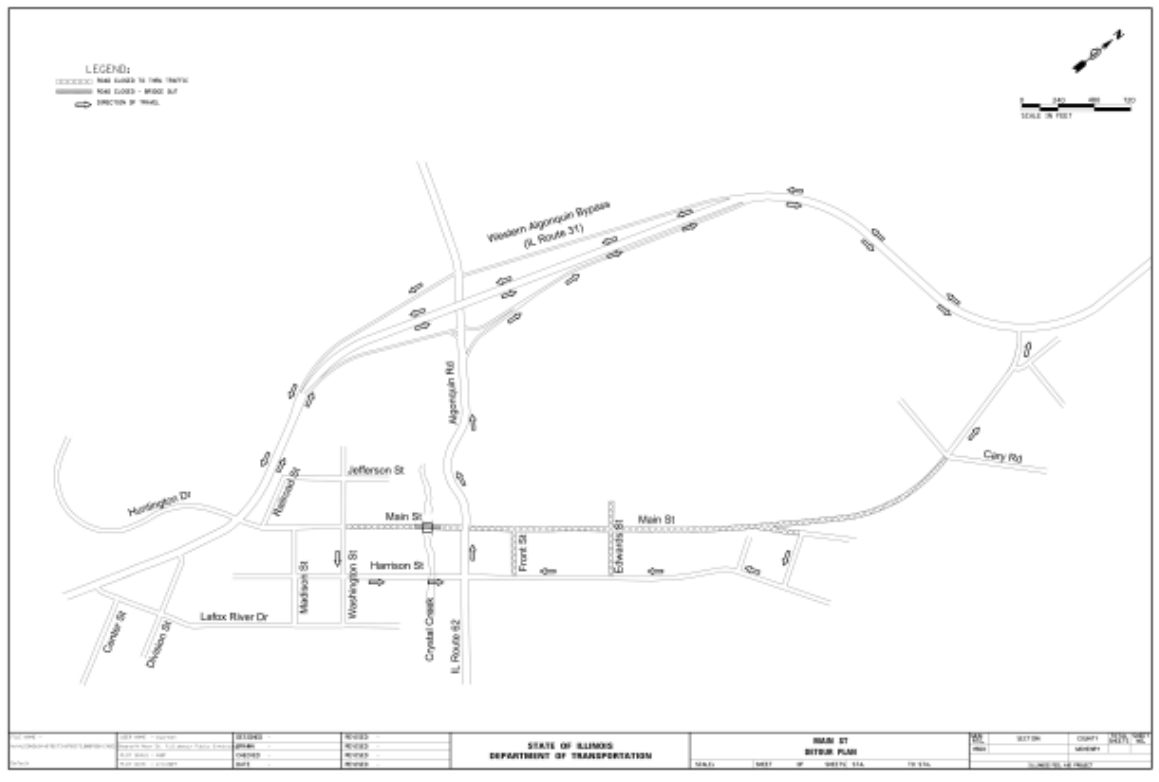

Please share the detour map, which can be found on the [project website](#), with your customers, employees and delivery drivers. As a reminder, the village parking lot at Harrison and Washington streets is available for workers, businesses and visitors.

For more information and the latest detour map, visit the [Old Town project website](#).
