



## Construction Update for the Week of June 10



The construction team is thrilled to announce drilling is complete for the new shaft foundations at Crystal Creek. We appreciate everyone's patience during this process. The next step in construction is the installation of concrete retaining walls and abutments for the bridge.

As a reminder, crews hope to finish bridge construction this summer and will then begin installing the pedestrian covered walkways along the bridge along with the steel archway.

This week, new irrigation systems will be installed in the planting beds along Main Street in the downtown area. The irrigation system allows water and nutrients to flow through the soil to help plants flourish.




---

Construction on the north section of Main Street is nearing completion! Crews will re-stripe the roadway now that patching is complete and, **weather permitting**, the road will be reopened to all traffic on Wednesday.



The current detour impacting the section of Main Street north of Algonquin Road will end this week and this section of the roadway will be reopened to all traffic. The [project website](#) will be updated with the latest detour maps when this change goes into effect.

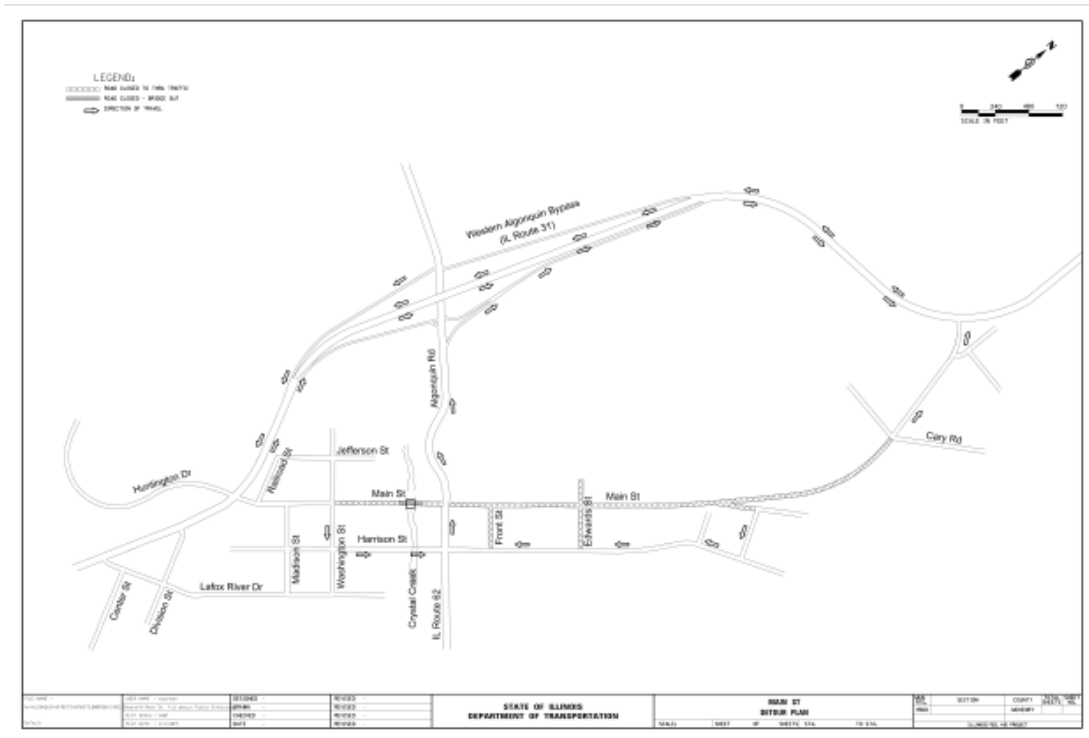

For more information and the latest detour map, visit the [Old Town project website](#).
