



Construction Update for the Week of June 3



While the wet spring has not been ideal, crews have continued to work and installed the center pier support for the bridge structure and finished drilling the shaft foundations on the south side. Crews will begin the same drilling process for the shaft supports on the north side. The drilling has also been completed on the shafts for the north abutments or ends of the bridge.

As a reminder, crews hope to finish bridge construction this summer and will then begin installing the pedestrian covered walkways along the bridge along with the steel archway.




The plaza outside of Historic Village Hall is ready for visitors. The new features in the plaza include:

- Flags flying over the stage area
- Colorful flower baskets
- The outdoor fireplace
- New tables, chairs and bench walls

- Decorative railings
- Festive lighting

On the north section of Main Street, crews have completed installing the new sanitary sewers. Construction is now focused on patching the roadway.

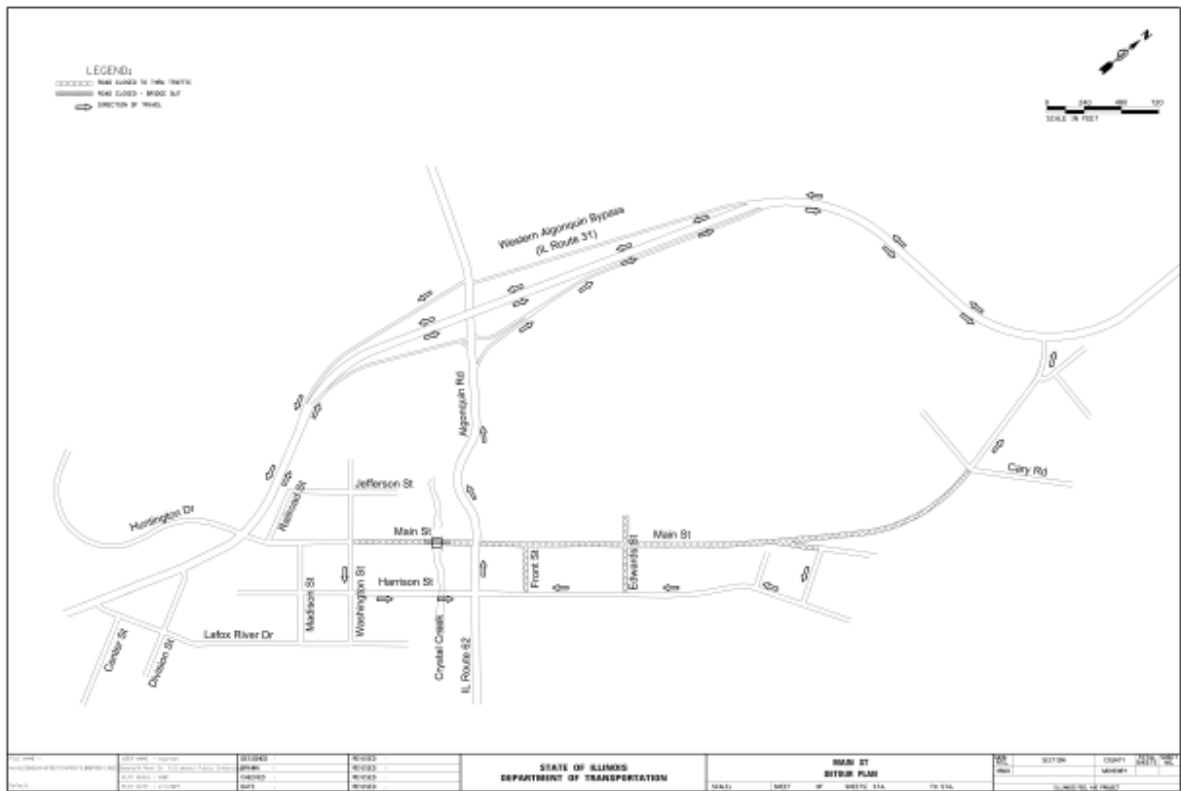

Please share the detour map, which can be found on the [project website](#), with your customers, employees and delivery drivers. As a reminder, the village parking lot at Harrison and Washington streets is available for workers, businesses and visitors.

For more information and the latest detour map, visit the [Old Town project website](#).

