



Construction Update for the Week of July 1



Progress continues to be made on installing the substructure of the bridge. This week, crews will continue the process of pouring concrete and forming the south abutments for the bridge.

Please note that due to the high temperatures and humidity anticipated for the week, crews have received approval to alter construction hours. Crews will **begin operations at 5 a.m. this week** due to the necessity of pouring concrete between certain temperatures. The Illinois Department of Transportation (IDOT) mandates that concrete temperatures remain below 90 degrees to allow concrete to set properly.




Sewer work north of the bridge will also begin this week. New sewer infrastructure was installed south of the bridge prior to the new roadway installation.

New asphalt driveways will also be placed on the north section of Main Street this week.



The current detour impacting the section of Main Street south of Algonquin Road remains in place during bridge construction.

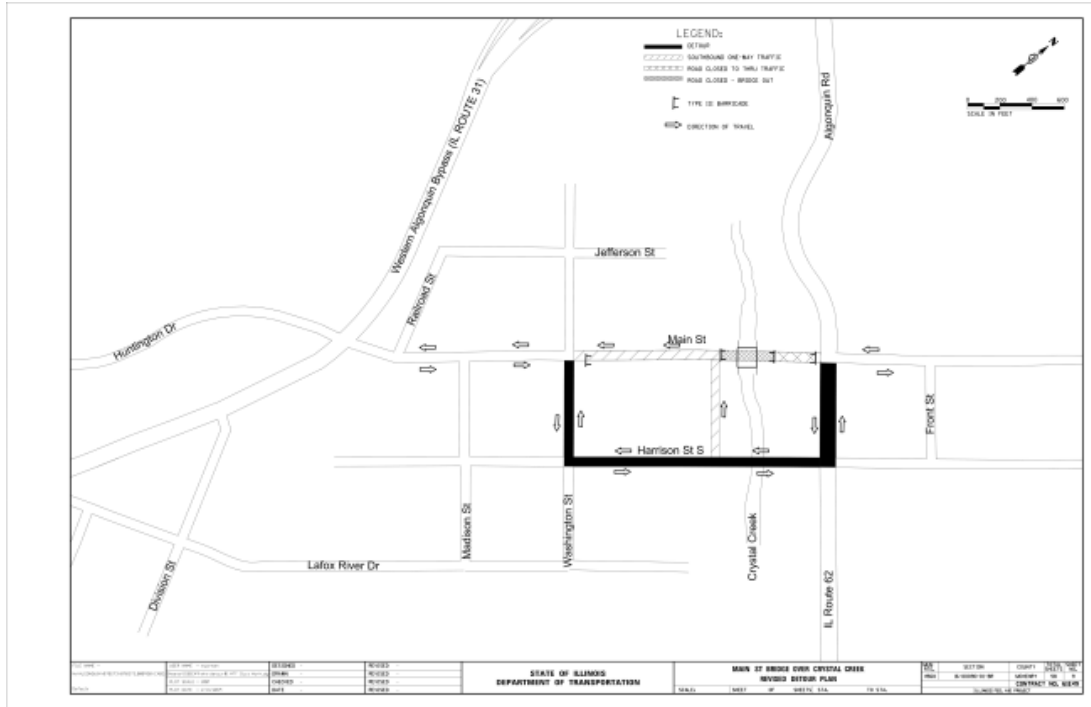

For more information and the latest detour map, visit the [Old Town project website](#).
