




Construction Update for the Week of March 23

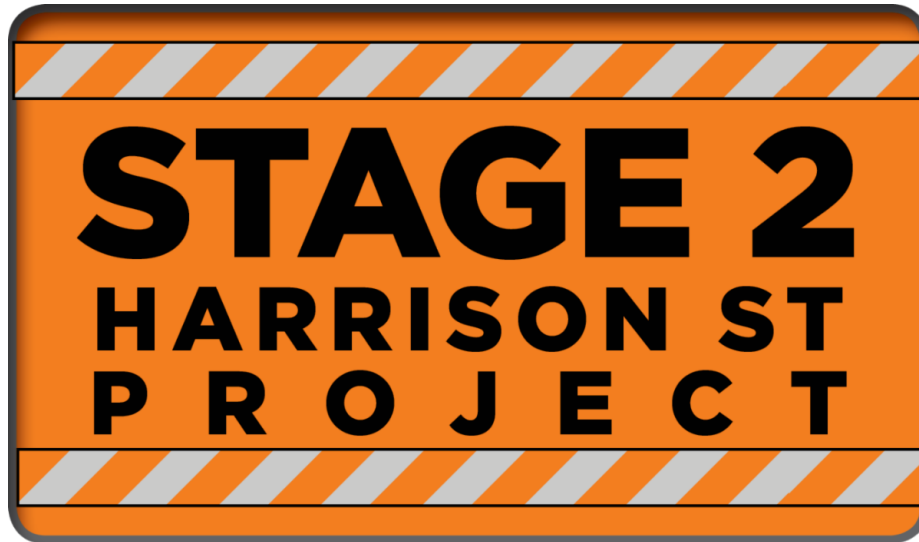

The Governor's stay-at-home order does not impact construction work; Harrison Street construction will continue as planned to ensure the safety and maintenance of our public infrastructure .

Last week, crews completed the storm sewer work on North Harrison Street and started the storm sewer work on Edwards Street. Crews also started replacing curbs and sidewalks along North Harrison Street.

This week, crews will continue replacing storm sewers along Edwards Street, as well as replacing curbs and sidewalks along North Harrison Street, The contractor also anticipates that crews will begin replanting grass in the parkways this week.

Here's what to expect as we move forward with completing the project:

- North Harrison Street *south* of Sunny Drive will be patched with concrete once the storm sewer improvements are completed at the intersection of North Harrison Street and Sunny Drive.
- North Harrison Street will be completely repaved from Sunny Drive *north* to the 900 block of North Harrison Street.
 - In the next few weeks, crews will begin removing remaining pavement on North Harrison Street north from from Sunny Drive and preparing for new asphalt.
 - Crews will begin repaving and patching roads once asphalt plants open up for the season. Historically, this has been mid-April to mid-May.
 - Asphalt driveway replacement will be completed around the same time as road repaving.

- Crews will replace curbs that were removed or damaged during construction.

A special property access notice:

- Edwards Street will be closed while the work associated with the storm sewer replacement and pavement patching is being completed. During this time, residents should use Front Street or Algonquin Road to access North Harrison Street.
- The contractor will do their best to maintain access to residential driveways while completing the driveway, curb and sidewalk replacements. There may be times when residents will be required to park on street overnight while this work is being completed. The contractor will review this on a case by case basis and will notify residents of any driveway access restrictions. The Village Police Department has been notified that overnight on street parking may be required for residents that are impacted by these improvements.

As the Stage 2 Harrison Street Project nears completion, the Village would like to thank you for your patience and cooperation during construction.

*Fox 14 Marina is open during construction and accessible from the north, off Blackhawk Trail.

Detour Alert

The Stage 2 detour is in effect and is expected to remain in place for several weeks. North Riverview Drive between North Main and Park streets will be closed as part of the stage 2 detour. Access to residences and businesses within the work zone will be maintained.



For more information and the latest detour map, visit the [Old Town project website](#).

If you have questions, please contact the Resident Project Representative, Dan Gillespie at 847-346-2538 or by email at d.gillespie@trotter-inc.com.

