




Construction Update for the Week of March 30

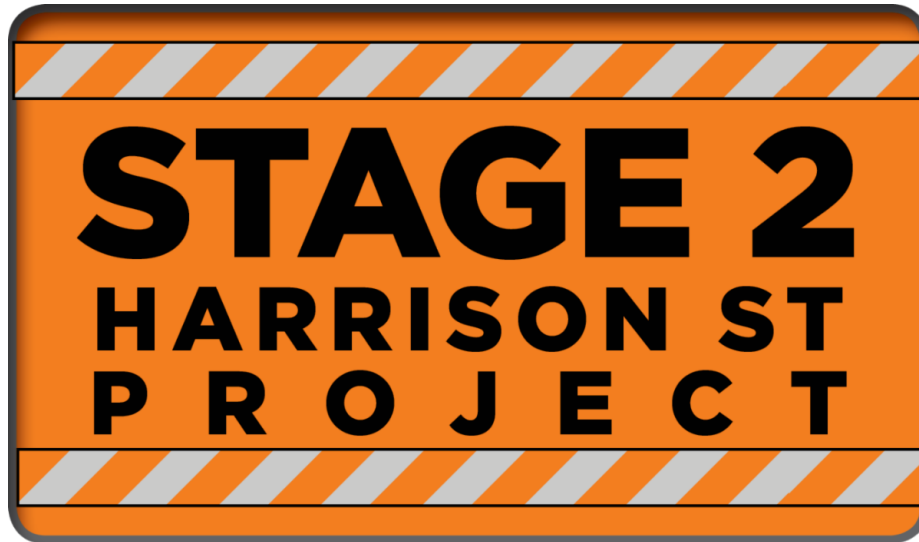

We are excited to announce that last week the contractor completed the storm sewer replacement! This completes the underground work for the project. Focus has now turned to restoration of the sidewalk, curb and roadway patching.

This week, residents will continue to see crews progress on the sidewalk, curb and roadway. It is anticipated that the parkway landscape restoration will begin this week as well.



Here's what to expect as we move forward with completing the project:

- North Harrison Street will be completely repaved from Sunny Drive *north* to the 900 block of North Harrison Street.
- In the next few weeks, crews will begin removing remaining pavement on North Harrison Street north from from Sunny Drive and preparing for

new asphalt.

- Crews will begin repaving and patching roads once asphalt plants open up for the season. Historically, this has been mid-April to mid-May.
- Asphalt driveway replacement will be completed around the same time as road repaving.

As the Stage 2 Harrison Street Project nears completion, the Village would like to thank you for your patience and cooperation during construction.

*Fox 14 Marina is open during construction and accessible from the north, off Blackhawk Trail.

Detour Alert

The Stage 2 detour is in effect and is expected to remain in place for several weeks. North Riverview Drive between North Main and Park streets will be closed as part of the stage 2 detour. Access to residences and businesses within the work zone will be maintained.



For more information and the latest detour map, visit the [Old Town project website](#).

If you have questions, please contact the Resident Project Representative, Dan Gillespie at 847-346-2538 or by email at d.gillespie@trotter-inc.com.
