




## Construction Update for the Week of October 21

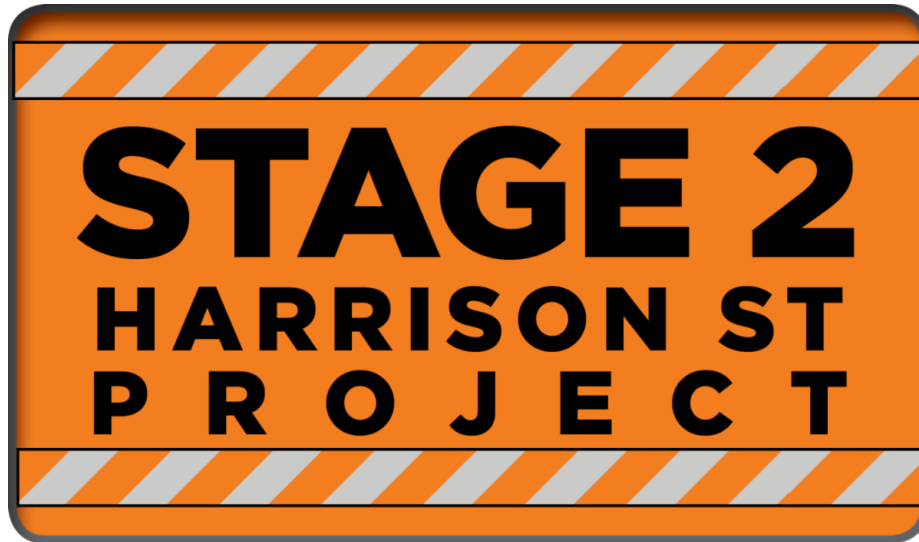

Last week, crews completed the installation and testing of the mainline sewer along North Harrison between Front and Edwards streets. The process of transferring the existing sanitary services to the new main line sanitary sewer began. Weather permitting, all underground work in the stage 1 work zone should be finished by mid-week.

This week, patching of the roadway, sidewalk and driveways in the stage 1 work zone will be complete. Upon completion, the stage 2 detour will go into effect by the end of the week. Once the stage 2 detour is in place, residents and businesses within the stage 1 work zone will have unrestricted access to their properties from Front Street up to the intersection of Edwards Street.

By the end of next week, the installation of the main line sewer within the stage 2 work zone will begin at the intersection of North Harrison and Edwards streets progressing north along North Harrison Street up to about 926 North Harrison Street. This work is expected to last several weeks.

After the main line sanitary sewer work is complete, various water shutoff valves and storm sewer lines will be replaced. New sanitary services will be installed for the properties along North Harrison Street. These improvements will impact several driveway entrances along the project route. These impacts and a timeline for the work will be provided in future updates as construction progresses.

### Here are some important things to expect for the stage 2 work zone area:

- Vehicles within the work zone are limited to the local residents within this zone and

those on Sunny Drive, Park Avenue, Brook Street and Riverview Drive. **General traffic should follow the detour routes.**

- The construction team will occupy a portion of the stage 2 work zone each day known as the **Immediate Work Area**. These areas will be marked by traffic control devices on either side of the work area.
- Vehicles will not be permitted through the Immediate Work Area during working and non-working hours.
- During working hours, residents within the Immediate Work Area may not have vehicular access to their properties. During these times, residents should park along North Harrison Street, south of the Immediate Work Area. Access will be restored to all properties at the end of each work day.
- During non-working hours, residents within the Immediate Work Area will have full access to their properties.
- Residents within the stage 2 work zone should plan their routes accordingly.
- All residents north of the Immediate Work Area should access their property from the north and all residents south of the Immediate Work Area should access their property from the south.

\*Please note, the parking lot for Riverfront Park will be closed until further notice for use by the contractor. Vehicles will not be able to access this area.

---

### Detour Alert

The Stage 2 detour plan will go into effect by the end of next week . The detour is expected to remain in place for several weeks. North Riverview Drive between North Main and Park streets will be closed as part of the stage 2 detour. Access to the residents and businesses within the work zone will be maintained.



---

**For more information and the latest detour map, visit the [Old Town project website](#).**

If you have questions, please contact the Resident Project Representative, Dan Gillespie at 847-346-2538 or by email at [d.gillespie@trotter-inc.com](mailto:d.gillespie@trotter-inc.com).

---

