




Construction Update for the Week of December 16

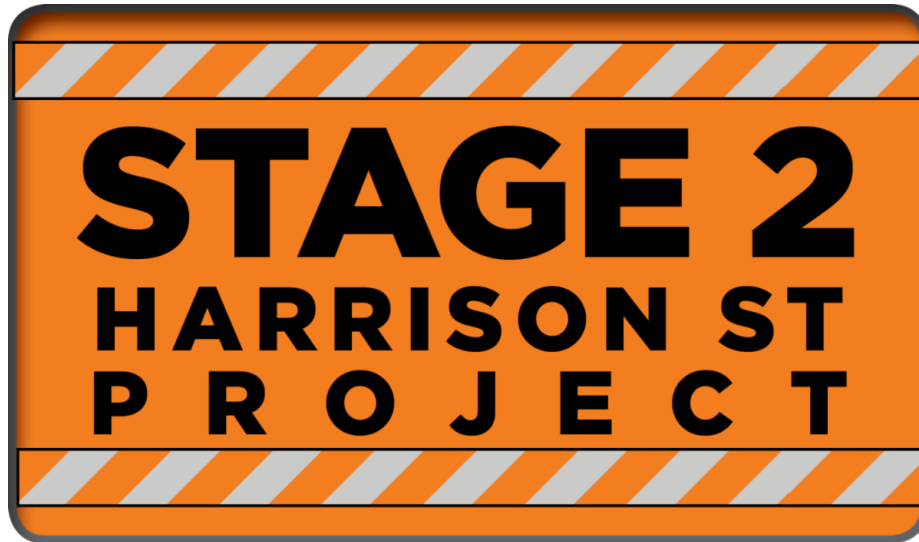

Last week, crews continued to install new mainline sewer along the 600 block of North Harrison Street.

This week, the contractor will continue with mainline sewer installation. It's anticipated the mainline sewer will be installed up to Park Street by the end of the week.

As work progresses over the next several weeks, the Village anticipates that the contractor will spend Saturdays completing sanitary service connections - the underground pipes that carry wastewater from your home to the sewer system - for properties along Harrison Street where the mainline sewer has been installed. Since several of these sanitary sewer connections are within driveways, access may be limited during this time. If this occurs, the Village asks that residents park on side streets. Thank you for your cooperation.

A special notice for properties along North Harrison Street:

- All residents south of the construction should continue to access their properties off North Harrison Street from Algonquin Road or Front Street.
- Residents to the north of this work zone and all other traffic should continue to follow the detour.

*Fox 14 Marina is open during construction and accessible from the north, off Blackhawk Trail.

The Stage 2 detour is expected to remain in place for several weeks. North Riverview Drive between North Main and Park streets will be closed as part of the stage 2 detour. Access to residences and businesses within the work zone will be maintained.



For more information and the latest detour map, visit the [Old Town project website](#).

If you have questions, please contact the Resident Project Representative, Dan Gillespie at 847-346-2538 or by email at d.gillespie@trotter-inc.com.
