




## Construction Update for the Week of Jan. 6

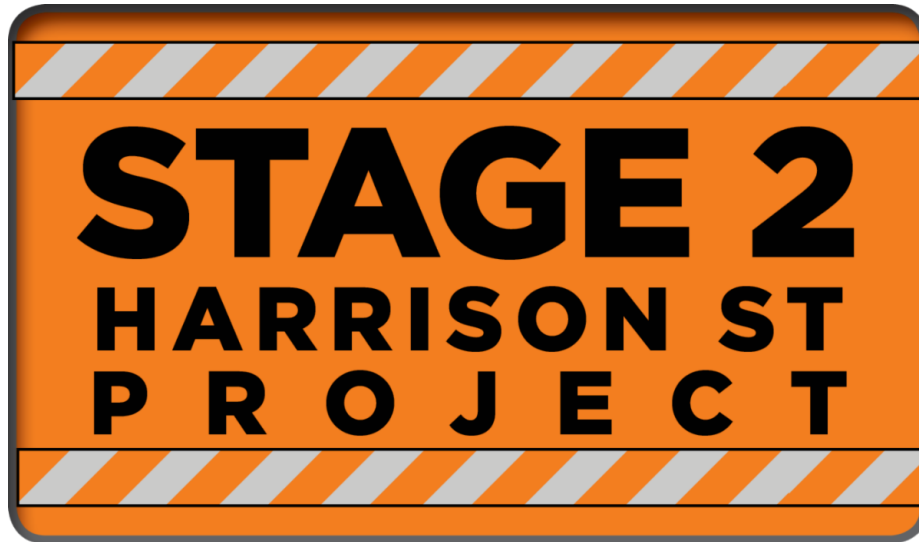

Last week, crews resumed construction of the mainline sanitary sewer along North Harrison Street, starting at the intersection of Park Street progressing north. The Stage 2 detour has been reinstated now that work has resumed.

This week, the contractor will continue with the installation of the mainline sanitary sewer along the 700 block of North Harrison Street.

As work progresses over the next several weeks, the Village anticipates that the contractor will spend Saturdays completing sanitary service connections - the underground pipes that carry wastewater from your home to the sewer system - for properties along Harrison Street where the mainline sewer has been installed. Since several of these sanitary sewer connections are within driveways, access may be limited during this time. If this occurs, the Village asks that residents park on side streets. Thank you for your cooperation.

### **A special notice for properties along North Harrison Street:**

- All residents along Sunny Drive, Park Street and those along North Harrison Street whose homes are *south* of Park Street should access their properties from Algonquin Road or Front Street.
- All residents along Brook Street and those along North Harrison Street whose homes are *north* of Park Street should continue to follow the detour to access their properties.

\*Fox 14 Marina is open during construction and accessible from the north, off Blackhawk Trail.

