




Construction Update for the Week of April 20

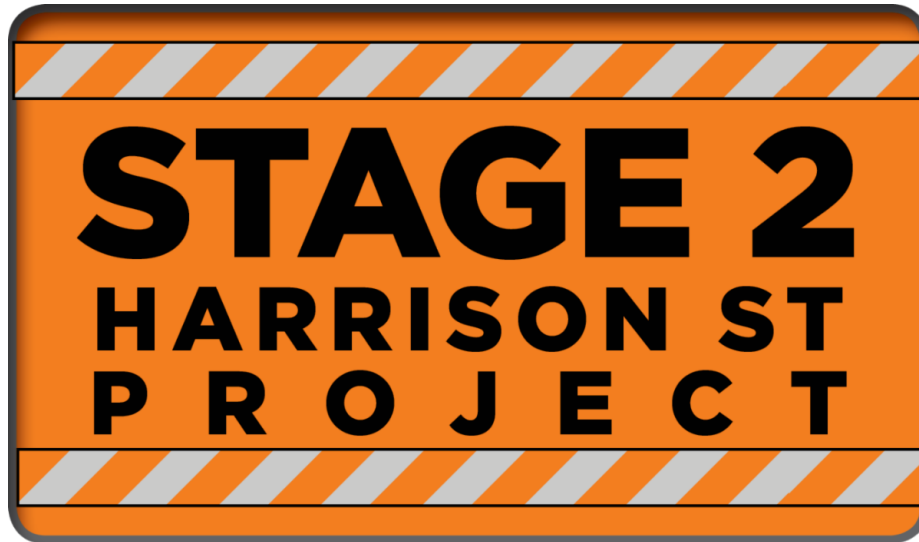

Last week, crews finished all sidewalk, curb and concrete driveway repairs and the contractor completed preparatory work for repaving North Harrison Street north of Sunny Drive. This repaving work is tentatively scheduled to begin this week, weather and conditions permitting. The Stage 2 Detour will remain in place during repaving and residents whose driveways will be replaced will need to temporarily park on the street.

As the Stage 2 Harrison Street Project nears completion, the Village would like to thank you for your patience and cooperation during construction!

Here's what to expect as we move forward with completing the project:

- North Harrison Street will be completely repaved from Sunny Drive *north* to the 900 block of North Harrison Street.
 - Asphalt driveway replacement will be completed around the same time as road repaving.
 - Parkway restoration will be finalized after the roadway work is completed.

*Fox 14 Marina is open during construction and accessible from the north, off Blackhawk Trail.

Detour Alert

The Stage 2 detour is in effect and is expected to remain in place for several

weeks. North Riverview Drive between North Main and Park streets will be closed as part of the stage 2 detour. Access to residences and businesses within the work zone will be maintained.



**For more information and the latest detour map, visit the
[Old Town project website.](#)**

If you have questions, please contact the Resident Project Representative,
Dan Gillespie at 847-346-2538 or by email at d.gillespie@trotter-inc.com.
