




Construction Update for the Week of April 6

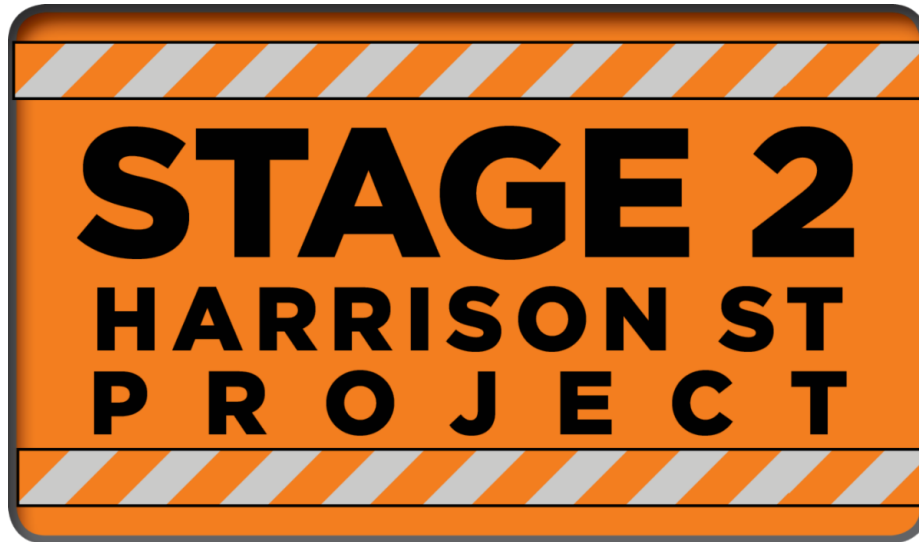

Last week, crews completed the sidewalk, curb and concrete driveway replacements, as well as began preparation work for restoring the parkway grass.

This week, residents will continue to see progress on the parkway landscape restoration as well as preparation for the asphalt driveway replacements which are anticipated to be completed next week.

Here's what to expect as we move forward with completing the project:


- North Harrison Street will be completely repaved from Sunny Drive *north* to the 900 block of North Harrison Street.
 - In the coming weeks, crews will begin removing remaining pavement on North Harrison Street north from from Sunny Drive and preparing for new asphalt.
 - Crews will begin repaving and patching roads once asphalt plants open up for the season. Historically, this has been mid-April to mid-May.
 - Asphalt driveway replacement will be completed around the same time as road repaving.

As the Stage 2 Harrison Street Project nears completion, the Village would like to thank you for your patience and cooperation during construction.

*Fox 14 Marina is open during construction and accessible from the north, off Blackhawk Trail.

Detour Alert

The Stage 2 detour is in effect and is expected to remain in place for several weeks. North Riverview Drive between North Main and Park streets will be closed as part of the stage 2 detour. Access to residences and businesses within the work zone will be maintained.

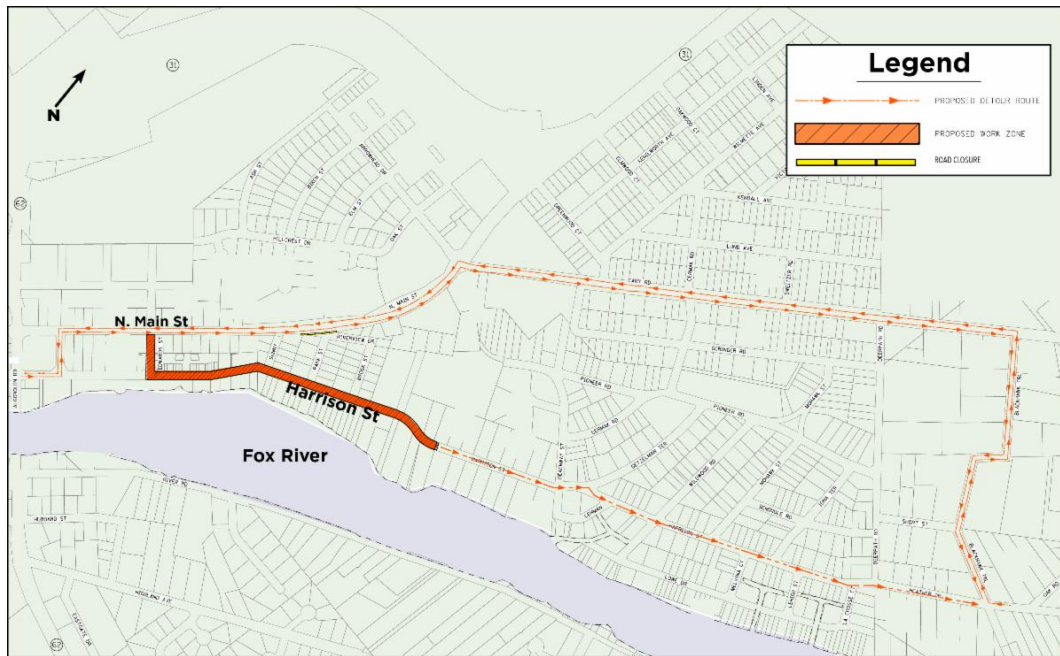

**For more information and the latest detour map, visit the
[Old Town project website.](#)**

If you have questions, please contact the Resident Project Representative,
Dan Gillespie at 847-346-2538 or by email at d.gillespie@trotter-inc.com.
