



## Construction Update: January 16

### Here's what crews accomplished this week:

- Finished placing the retaining wall along RT 31 by the lift station wet well.
- Completed water main pressure testing and chlorination.
- Disconnected the electrical service and relocated the street lighting at the River Front Lift Station at the intersection of N. Harrison and Front streets.

### Here are the contractor's plans for next week:

- Conclude all underground water main work within the roadway on La Fox River Drive and Center Street, which includes the following:
  - Finish connecting the final two water mains to the existing water main.
  - Complete installation of water services.
- Complete removal and abandonment of the River Front Lift Station.
- Have the control building for the lift station delivered and set on the building foundation.
- Pour the concrete pad\* of the odor control system for the lift station.

\*Base on which the unit will sit


---

### Detours and Closures

La Fox River Drive between RT 31 and Center Street as well as Center Street north of La Fox River Drive remain closed.

Please refer to the map below to detour around the closures. Thank you again for your continued cooperation and patience.

---

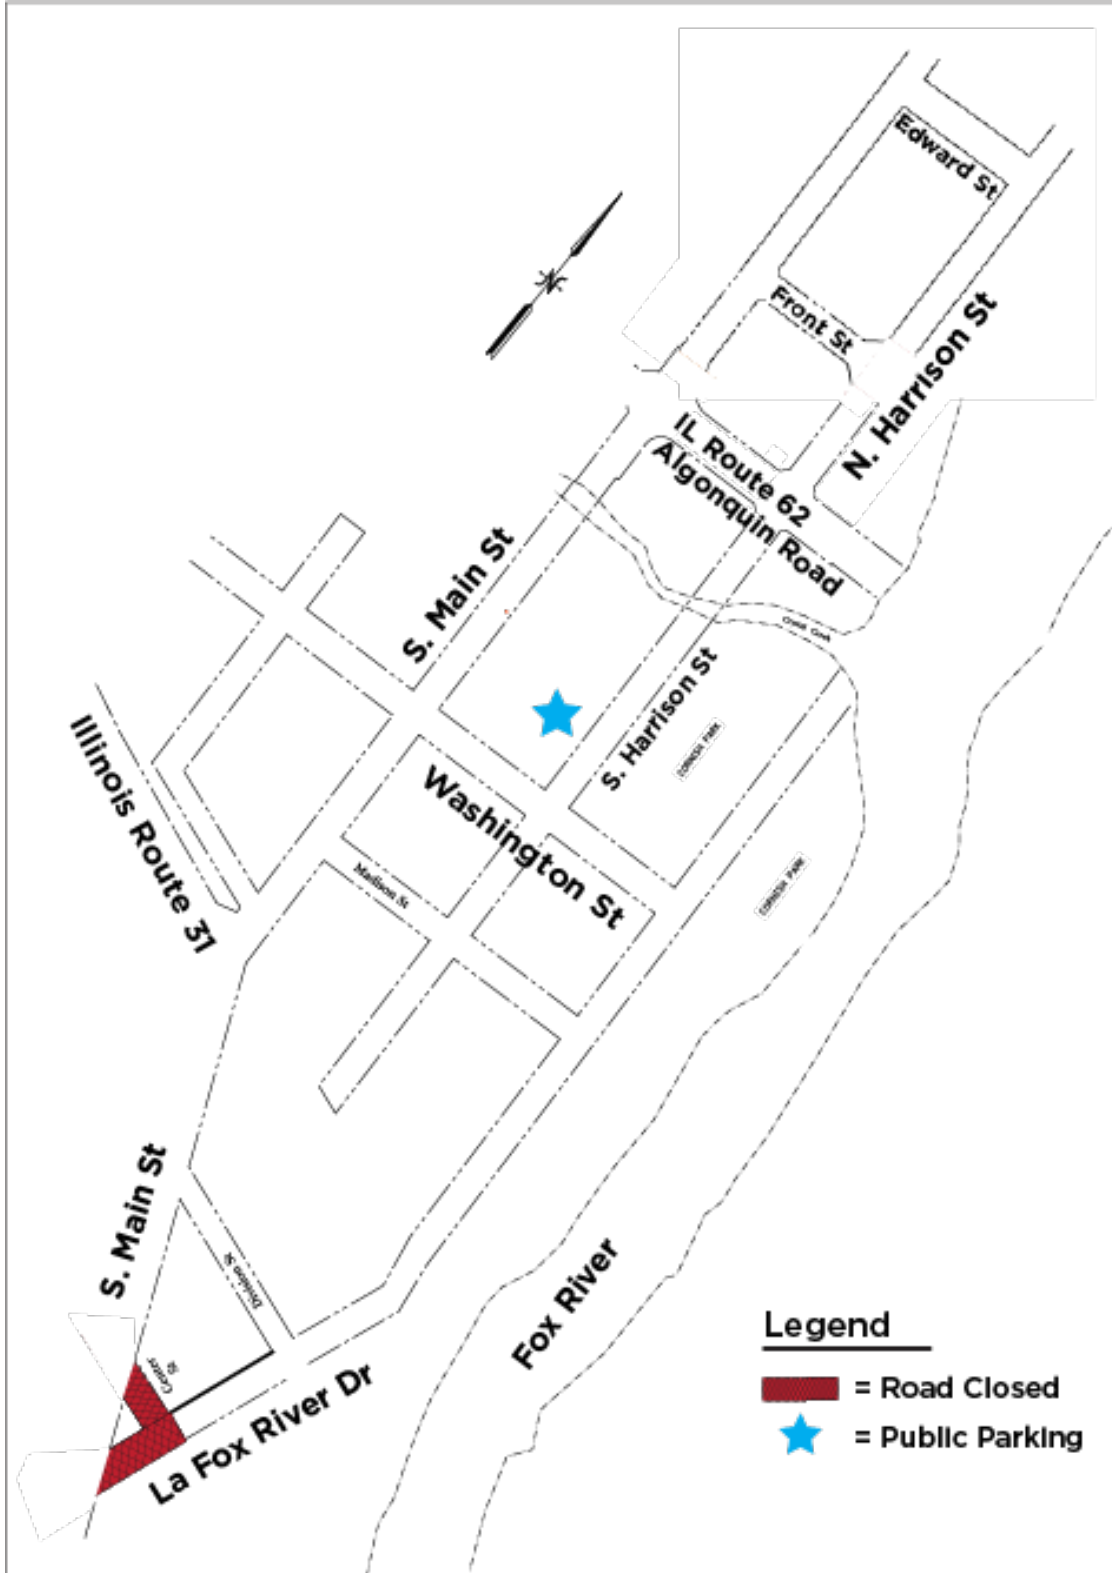

Visit Our Project Website

If you have questions or concerns contact Dan Gillespie at (847) 346-2538 or via email [d.gillespie@trotter-inc.com](mailto:d.gillespie@trotter-inc.com).
