



Construction Update: January 9

This week, crews made the following progress:

- Began water main installation on La Fox River Drive and Center Street near the lift station site.
- Finished installing the electrical conduit* for the lift station wet well.
- Cleaned up construction equipment and work area at the southwest corner of the intersection of Harrison Street and Algonquin Road.

*Tubing used to protect and route electrical wiring in a building.


Next week, the contractor will tackle the following projects:

- Begin placing the retaining wall along RT 31 by the lift station wet well.
- Complete removal and abandonment of the River Front Lift Station at the intersection of North Harrison and Front streets.
- Finish testing the water main installed on La Fox River Drive and Center Street. Crews will then begin the final connections between the newly installed and existing water mains.

Detours and Closures

- La Fox River Drive between RT 31 and Center Street as well as Center Street north of La Fox River Drive remain closed.

Please refer to the map below to detour around the closures. Thank you again for your continued cooperation and patience.

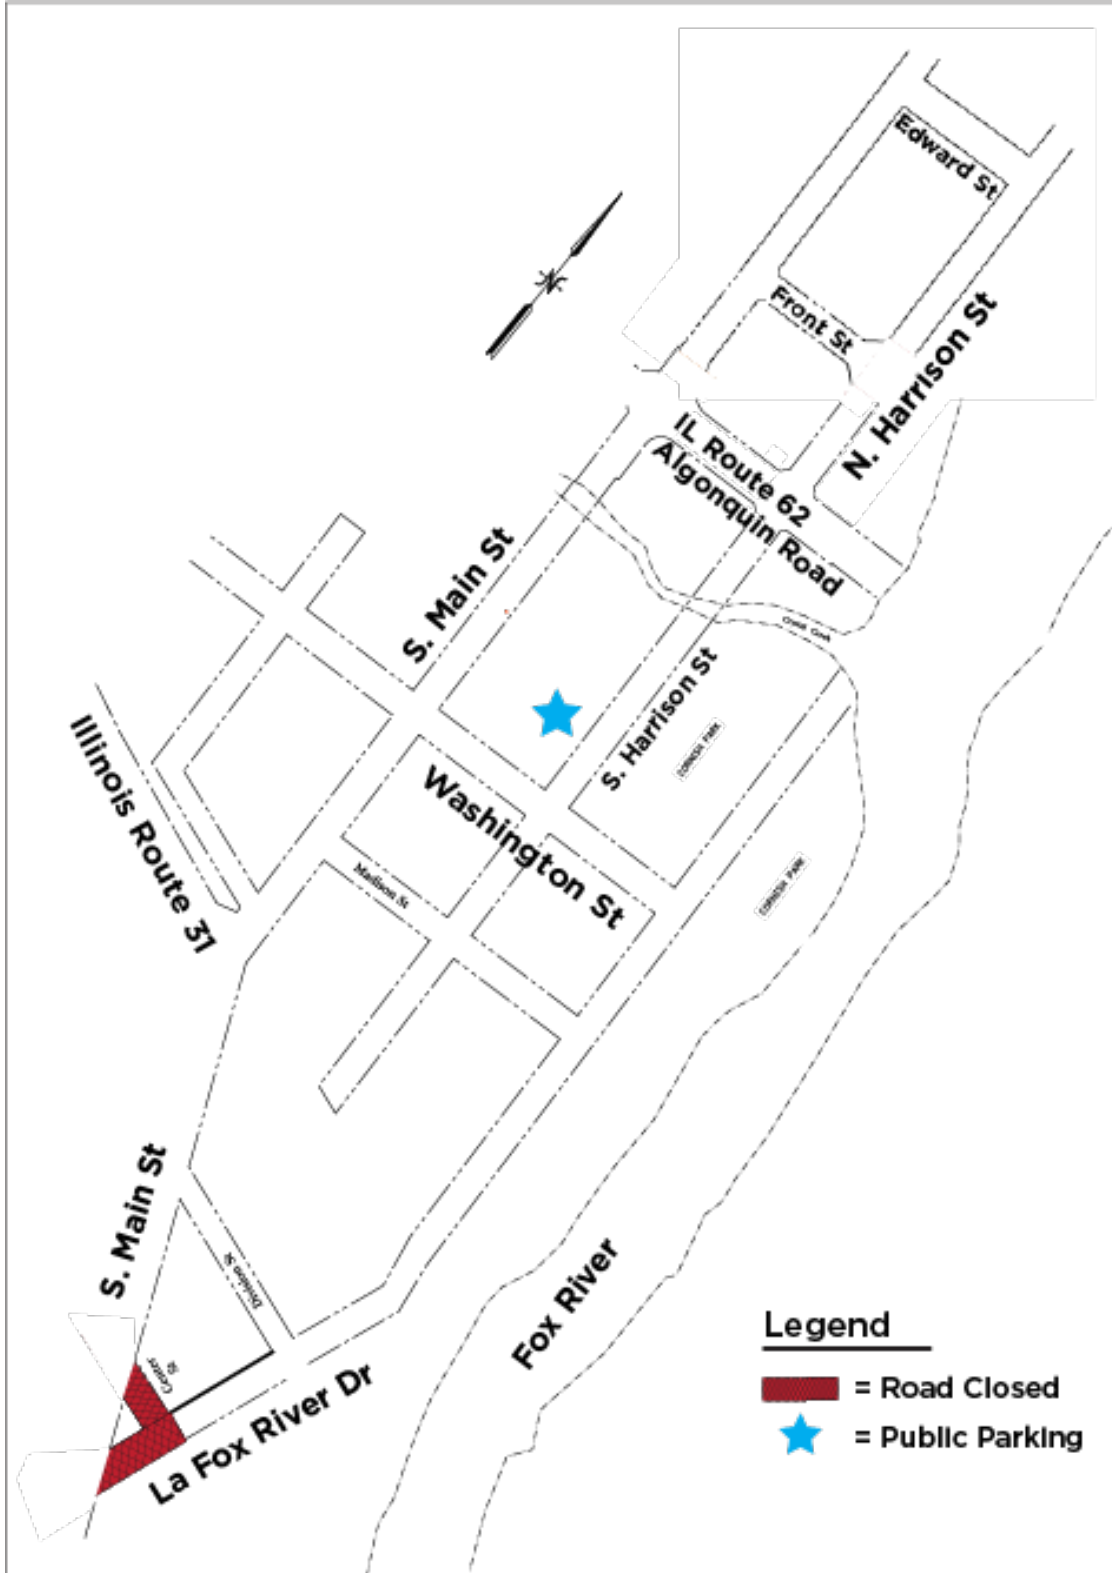

Visit Our Project Website

If you have questions or concerns contact Dan Gillespie at (847) 346-2538 or via email d.gillespie@trotter-inc.com.
