



Construction Update: December 19

This week, crews continued installing the sanitary sewer on La Fox River Drive near the lift station. The construction team also finished installing the electric service for the control building.

Next week, the contractor will begin installation of piping inside the lift station wet well. Additionally, crews will make the final connection to the existing sanitary sewer on Center Street - this will conclude all sanitary sewer work.


Note: Construction will pause between Thursday, December 24 and Sunday, December 27. Construction updates will resume after the New Year. Have a healthy, safe and happy holiday season!



Detours and Closures

- **N. Harrison Street is now open to traffic.**
- La Fox River Drive between RT 31 and Center Street as well as Center Street north of La Fox River Drive remain closed.

Please refer to the map below to detour around the closures. Thank you again for your continued cooperation and patience.

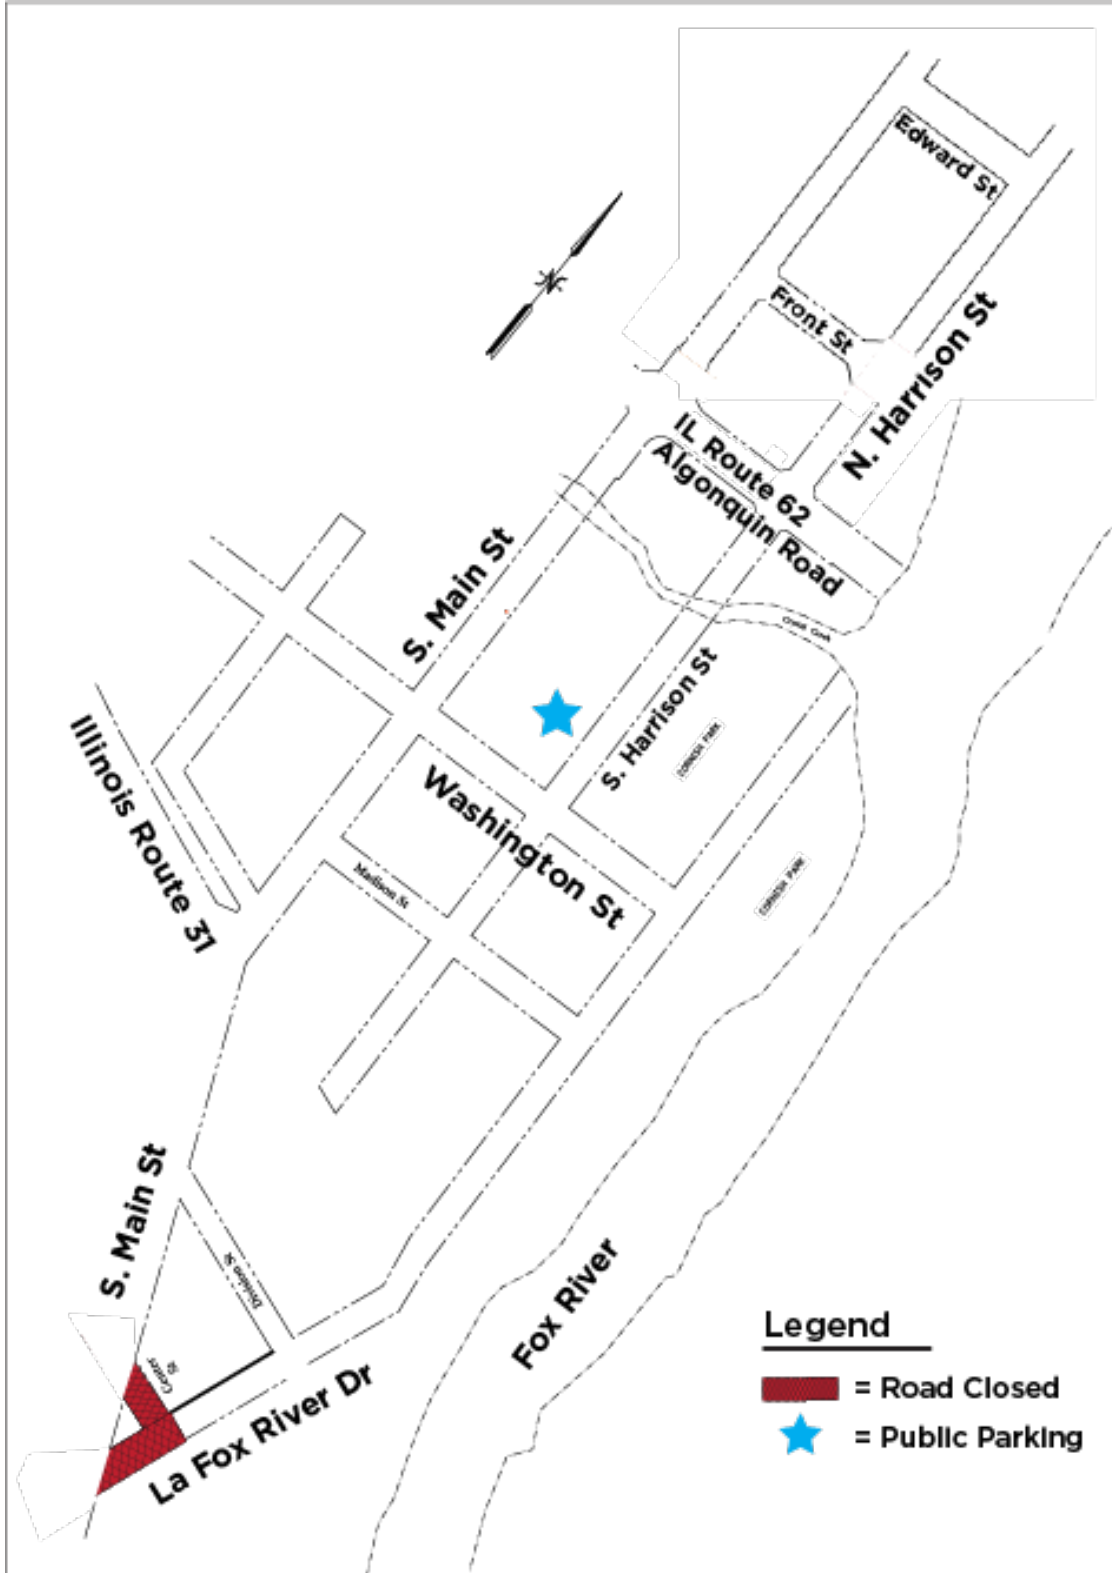

Visit Our Project Website

If you have questions or concerns contact Dan Gillespie at (847) 346-2538 or via email d.gillespie@trotter-inc.com.
