

Construction Update: February 6



Lift station control building brick veneer installation

This week, crews completed the removal and abandonment of the River Front Lift Station located at the intersection of N. Harrison and Front streets. Crews then began the installation of the brick veneer around the exterior of the control building (seen in the photo above). Additionally, the construction team completed the final underground connection to the existing sanitary sewer on Center Street. This concludes all underground utility work for the project!

Next week, the construction team will be working on the following projects:


- Finishing the installation of the brick veneer around the control building
- Completing the electrical work for the new lift station

*Due to extreme weather conditions predicted for next week, some work may be delayed.

Detours and Closures

La Fox River Drive between RT 31 and Center Street as well as Center Street north of La Fox River Drive **is open to local traffic only.**

Please refer to the map below to detour around the closures. Thank you again for your continued cooperation and patience.

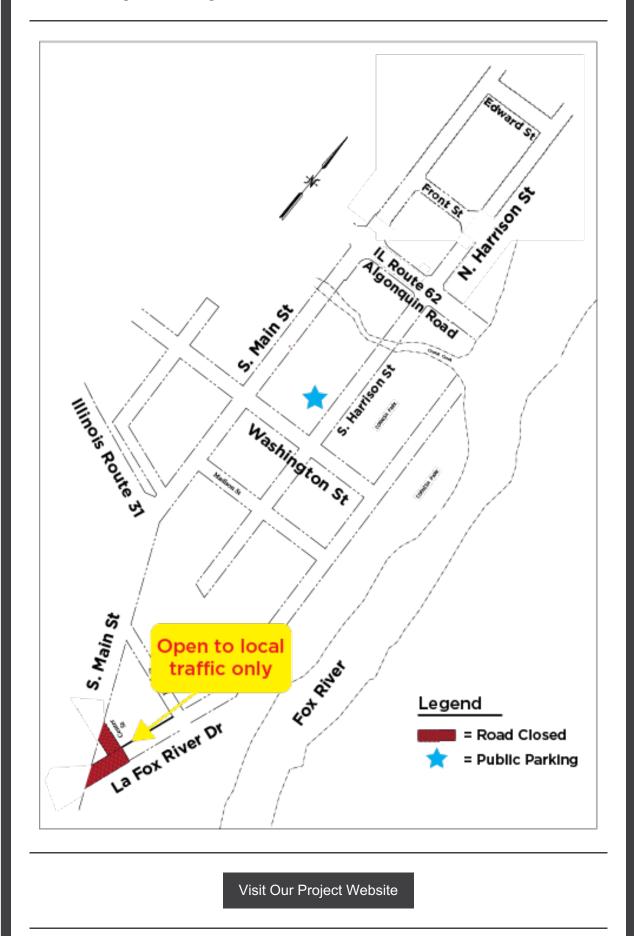

If you have questions or concerns contact Dan Gillespie at (847) 346-2538 or via email d.gillespie@trotter-inc.com.
