



Construction Update: April 4




Photos of similar dewatering well installation

This week, the contractor has begun installing a series of temporary wells that will lower the ground water elevation and keep trenches dry, allowing the utility work to occur. Installation of the wells should take approximately two weeks to complete. The contractor also removed trees and brush along Center Street this week.

Following the well installation, the contractor will install the sanitary sewer, most likely by April 20, but this is dependent on how long it takes to lower the ground water elevation. The sewer installation will start at the intersection of La Fox River Drive and Center Street and progress north.

Detour:

Traffic will be routed along Route 31 to Main Street and then back to Washington Street and La Fox River Drive.

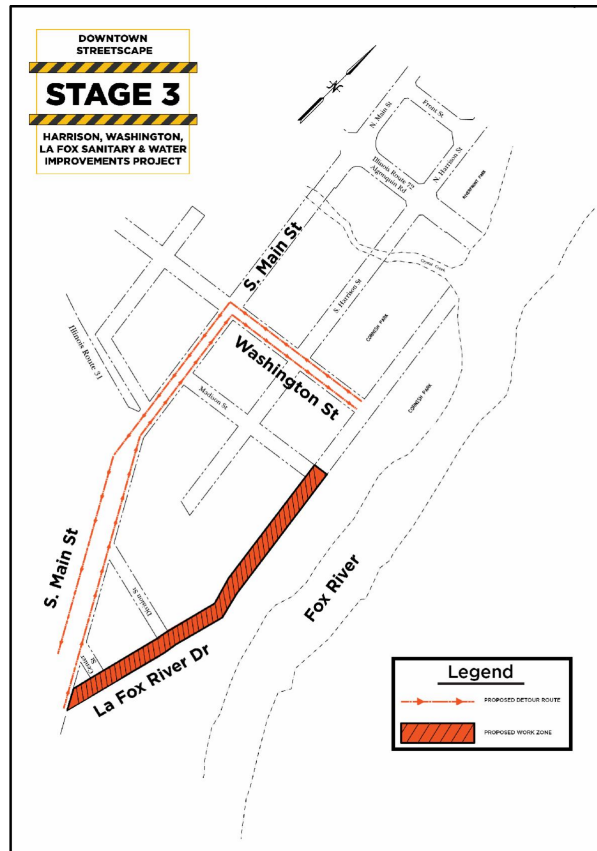

This project is expected to take 10 months to complete. We appreciate everyone's patience and understanding as we invest in this important infrastructure project to improve the community.

[Visit Our Project Website](#)

If you have questions or concerns contact Dan Gillespie at (847) 346-2538 or via email d.gillespie@trotter-inc.com.
