



Construction Update: July 18

This week, crews began installing the water main at Center Street and progressed north along La Fox River Drive.

Next week, the contractor expects to install the water main up to Madison Street. Crews will also continue installing temporary dewatering wells along South Harrison Street.

What's Next?


Crews will transfer water services to the new water main once the contractor has tested and disinfected it. Residents will experience a water disruption for a few hours during this transfer and will be notified 48-hours in advance.



Detour:

Traffic is being routed along Route 31 to Main Street and then back to Washington Street and La Fox River Drive.

We ask that drivers, pedestrians and bicyclists use caution due to the level of construction equipment along La Fox River Drive.

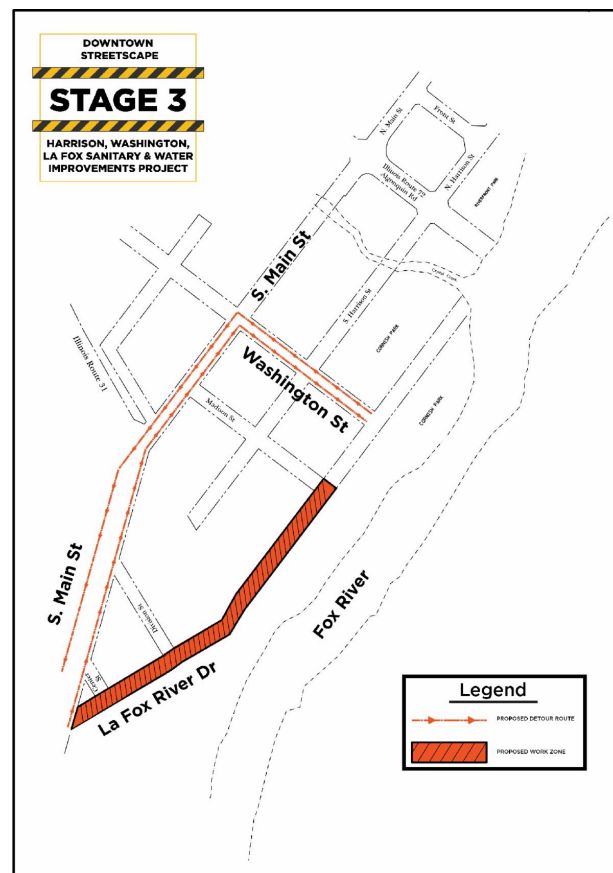

This project is expected to take approximately 10 months to complete. We appreciate everyone's patience and understanding as we invest in this important infrastructure project to improve the community.

[Visit Our Project Website](#)

If you have questions or concerns contact Dan Gillespie
at (847) 346-2538 or via email d.gillespie@trotter-inc.com.
