




## Construction Update for the Week of July 15



This past week, the work zone area around the bridge was back filled. The work zone area had been previously excavated to allow crews to work at the base of the creek during the construction of the new bridge substructure. Now that this work is complete the area was filled with construction material that will eventually support the new roadway on either side of the bridge.


Next week, the construction crews will begin removing the temporary cofferdam. The cofferdam is the metal structure that was used to contain the creek while the permanent bridge substructure was built. Once the temporary structure is removed, Crystal Creek will be directed through the new creek bottom. Additional work on the creek this week will include excavating and stream stabilization.

---



Old Town Algonquin is in full bloom! If you have not visited lately, stop by and check out the beautiful new features and new landscaping.

As a reminder, the current detour impacting the section of Main Street south of Algonquin Road remains in place during bridge construction.

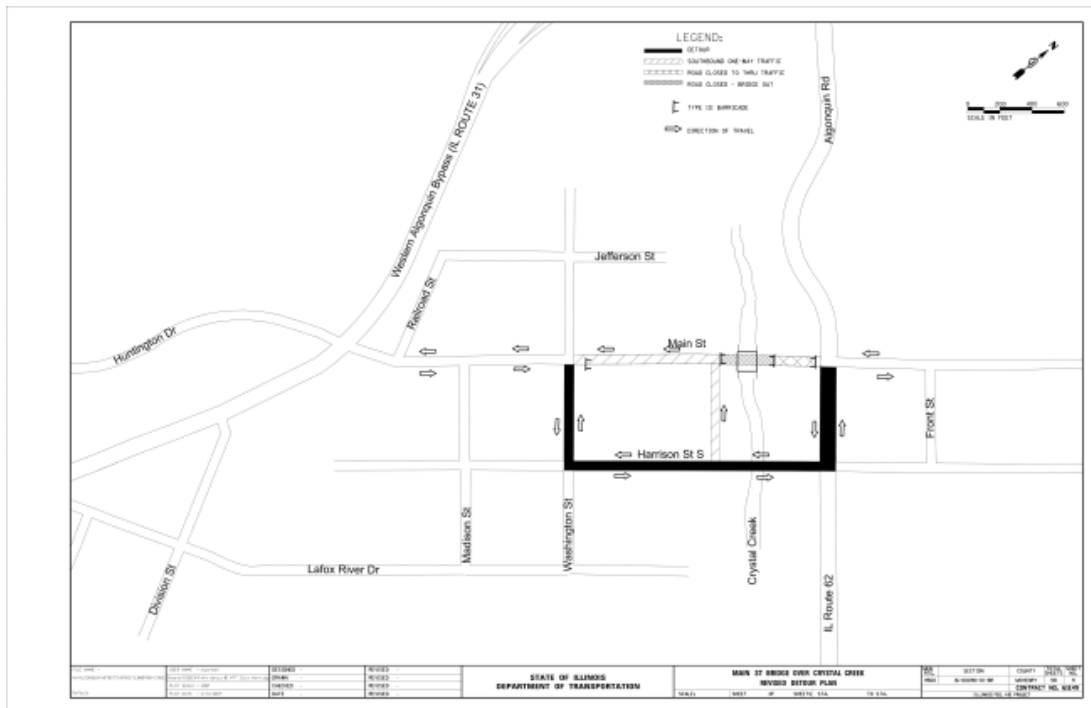

**For more information and the latest detour map, visit the [Old Town project website](#).**
