

Construction Update October 2, 2024

Stage Two Update:

The contractor continued brick paver installation on Harrison Street, placed concrete for the raised planter beds east on Harrison Street, and began planting trees on Harrison Street, from Route 62 to Washington Street.

Next week, the contractor will complete the brick paver installation on the east side of Harrison Street.

Stage Three Update:

The contractor removed curb and gutter along the south side of Washington Street and placed the new curb and gutter at the intersection of Washington and Harrison Streets. The contractor also removed the existing pavement on Washington Street and excavated for the new brick paver roadway.

Next week, the contractor will install the new underdrain on the south side of Washington Street and existing downspouts into the new storm sewer on the south side of Harrison Street. The contractor will also install the concrete base in preparation for placement of the new brick paver roadway at the intersection of Washington and Harrison Streets.

Harrison Parking Lot Update:

Over the last two weeks, the contractor completed the dumpster enclosures and installed conduit and handholes for the new parking lot lighting.

We are excited to see all the new elements come to life as we add the Old Town Algonquin charm to Washington and Harrison.






Brick paver installation on Harrison Street

Placing concrete on Harrison Street

As a reminder, this detour will remain in place until the end of

November.

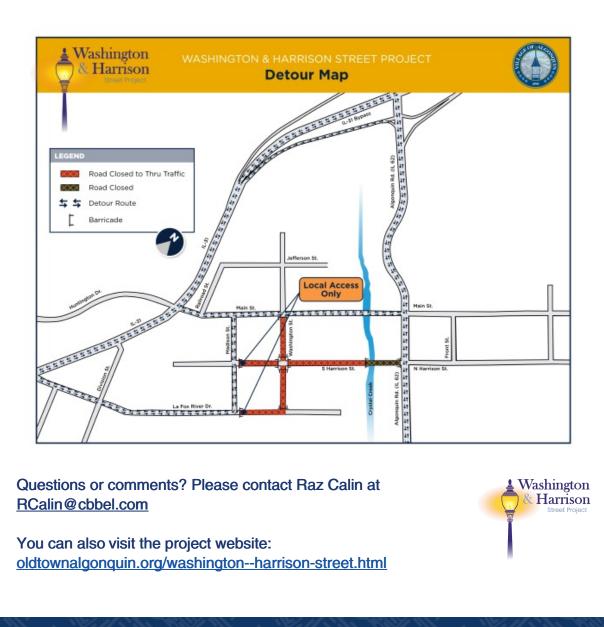

Metro Strategies Group, LLC. | 1901 Butterfield Road Suite 260 | Downers Grove, IL 60515 US

Unsubscribe | Update Profile | Constant Contact Data Notice



Try email marketing for free today!
