



## Construction Update for the Week of October 7




This week, crews were able to install the new brick pavers in the parking stalls between the bridge and Algonquin Road. The brick pavers match the ones installed on the south section of Main Street, adding additional character throughout the corridor.

Crews were also busy in this section of Main Street framing the roadway for the new concrete that was poured. The concrete will take seven days to cure or set before additional work can proceed. Please do not walk or drive over this surface during this time.


Once the concrete is complete, the new steel archway will be placed over Main Street adding to the charm of Old Town. In mid-October, after the archway is installed, the roadway will be reopened at Algonquin Road to southbound traffic.

---

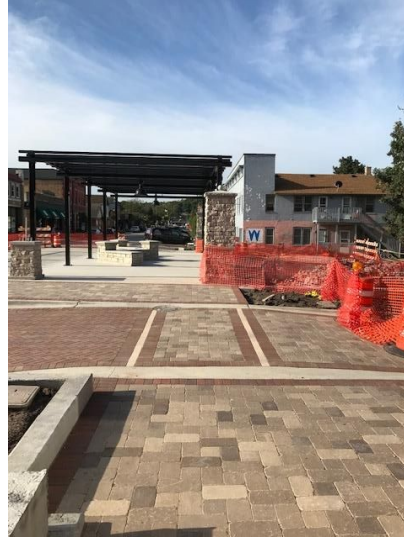

While crews complete the roadway construction on Main Street, handrails will be added to the retaining walls on the bridge this week to create a safe environment for pedestrians.

The current detour impacting the section of Main Street south of Algonquin Road remains in place until the roadway reopens. As a reminder, **public parking is available** along Main Street south of the bridge or in the parking lots located behind Bold American Fare Restaurant or at the corner of Harrison and Washington streets. The parking lot located behind Bold American Fare can be accessed directly from IL 62.

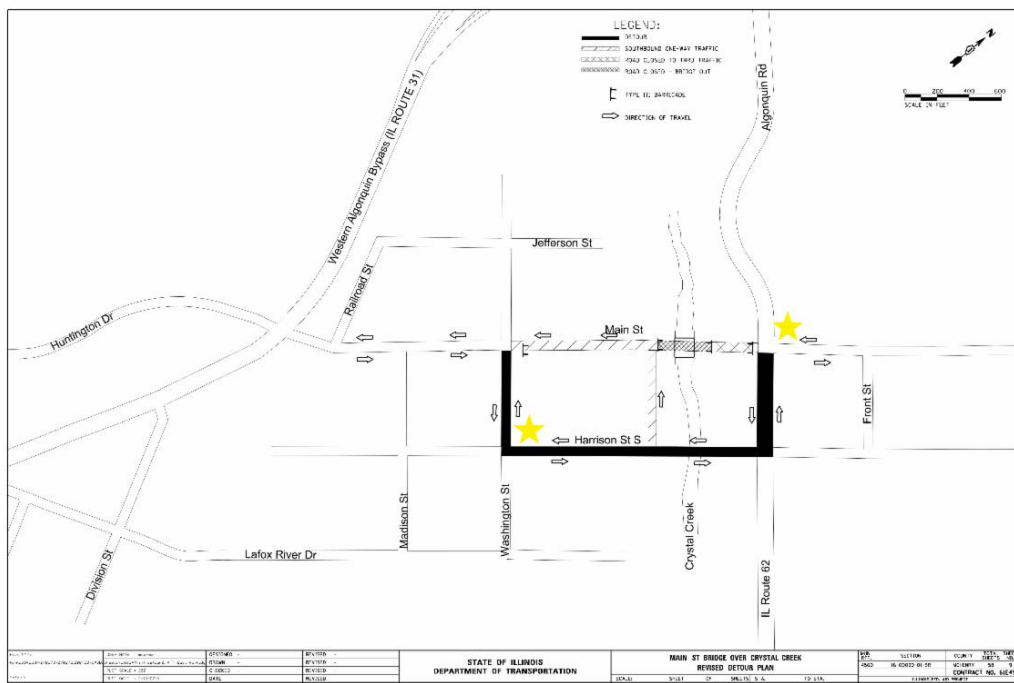

For more information and the latest detour map, visit the [Old Town project website](#).
