




Construction Update for the Week of October 14

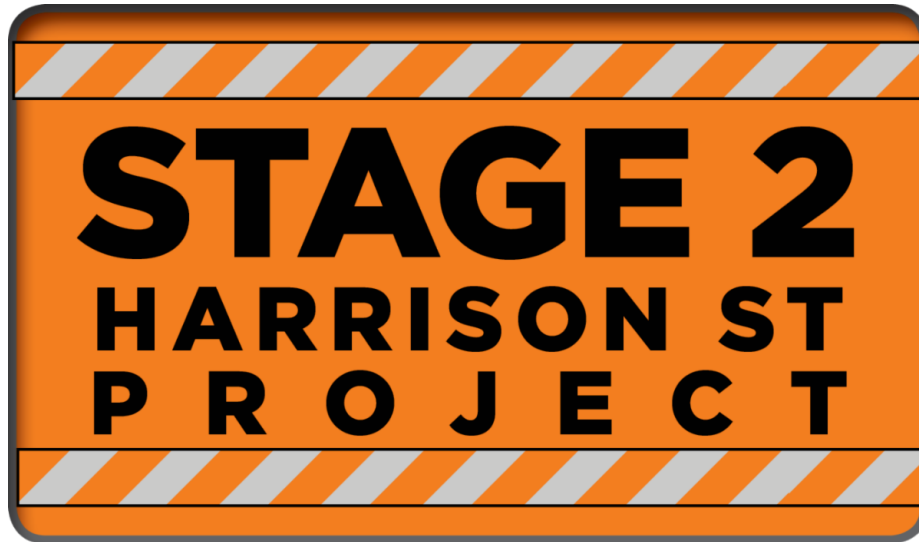

Last week, installation of the mainline sanitary sewer along North Harrison Street started. Crews made the connection to the existing lift station at Front Street and progressed north along North Harrison Street with the sewer installation.

Crews expect to make a lot of progress this week, as the mainline sewer installation in the stage 1 work zone is expected to be completed and ready for testing at the end of the week, contingent upon weather.

To allow for the portion of the work in the stage 1 work zone to be tested, crews will need to install the manhole at the intersection of North Harrison and Edwards streets. This manhole is outside of the current work zone. Flaggers will be utilized while workers are in the intersection.

Once testing is complete, the existing sanitary services will be transferred from the current sewer to the newly installed sewer. Crews will also replace fire hydrants and install a few new water services in the current work zone area. It is anticipated that the roadway patching will be completed in the coming weeks.

The stage 1 detour will remain in place and flaggers will be present to direct traffic for work outside the current detour. Please note that a new detour will be going in effect in the coming weeks as construction shifts north. Information about the detour will be posted on the Village's site, the project website and in the weekly construction update. As a reminder, North Riverview Drive between North Main and Park streets will be closed as part of the stage 2 detour.

Detour Alert

The Stage 1 detour plan is in effect. The detour is expected to remain in place until construction between Front and Edward streets is completed. Access to the residents and businesses within the work zone will be maintained.

Stage 1 Detour Map



For more information and the latest detour map, visit the [Old Town project website](#).

If you have questions, please contact the Resident Project Representative, Dan Gillespie at 847-346-2538 or by email at d.gillespie@trotter-inc.com.
